



More than just a Schedule Quality Tool


The full project team can benefit from XER Schedule Toolkit with shared access to view and analyse the project schedule



More than just a

Schedule Quality Tool

The full project team can benefit from XER Schedule Toolkit with shared access to view and analyse the project schedule

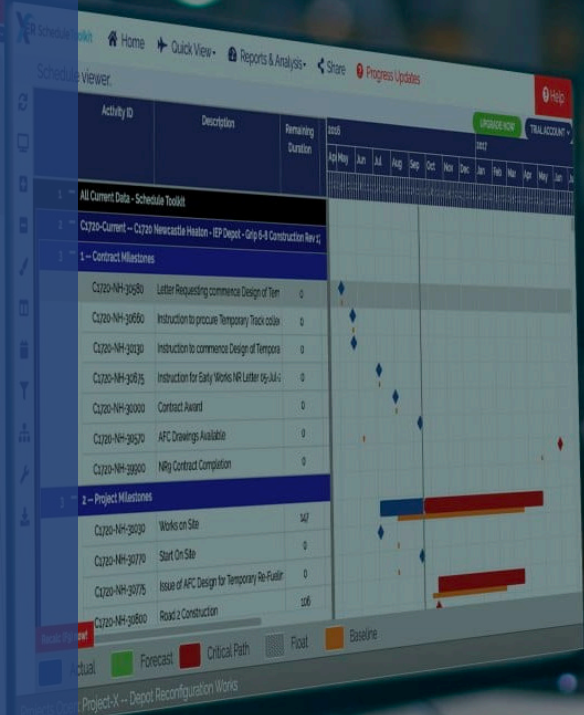

The screenshot shows the 'Schedule viewer' interface with a Gantt chart and a table of activities:


Activity ID	Description	Remaining Duration	Cost
1 - Contract Milestones			
C1720-NH-30580	Letter Requesting commencement Design of Tem	0	
C1720-NH-30560	Instruction to procure Temporary Track cabin	0	
C1720-NH-30430	Instruction to commence Design of Tempora	0	
C1720-NH-30475	Instruction for Early Works NR Letter (5-M-A)	0	
C1720-NH-30000	Contract Award	0	
C1720-NH-30570	AFC Drawings Available	0	
C1720-NH-30900	NRQ Contract Completion	0	
2 - Project Milestones			
C1720-NH-30030	Works on Site	147	
C1720-NH-30770	Start On Site	0	
C1720-NH-30775	Issue of AFC Design for Temporary Re-Fuel	0	
C1720-NH-30600	Road 2 Construction	116	

XER Schedule Toolkit is an all-in-one, third party toolkit that allows planners, schedulers and the wider project team to view, analyse and share Primavera P6, Microsoft Project and Asta Powerproject files.

Our software contains automation tools that help to enhance the planning process and ultimately drive improvements in the successful delivery of projects to time and budget.

Our cloud based solution provides planners & schedulers with a range of tools that allows them to automate day to day tasks, saving time and money whilst giving the full project team intelligent access to the schedule in a format they can understand and derive value from.

Trusted by our Corporate Partners Across the World



XER Schedule Toolkit enhances the planning process for a range of industries




Road & Railway



Oil & Gas




Aerospace &
Defence



Nuclear




Engineering &
Construction



View, analyse & share P6, MPP & Asta project schedules at the click of a button.

XER Schedule Toolkit provides a dynamic schedule reader that can be used to communicate the project's programme goals and objectives to the entire project team. Combined with the Toolkit's powerful share function, the toolkit ensures that everyone is always aligned to the latest version of the project schedule.

The schedule viewer can be structured and filtered similarly to Primavera P6, including by WBS and Activity Codes and layouts can be set up by individual users or by project controllers and shared across the team.

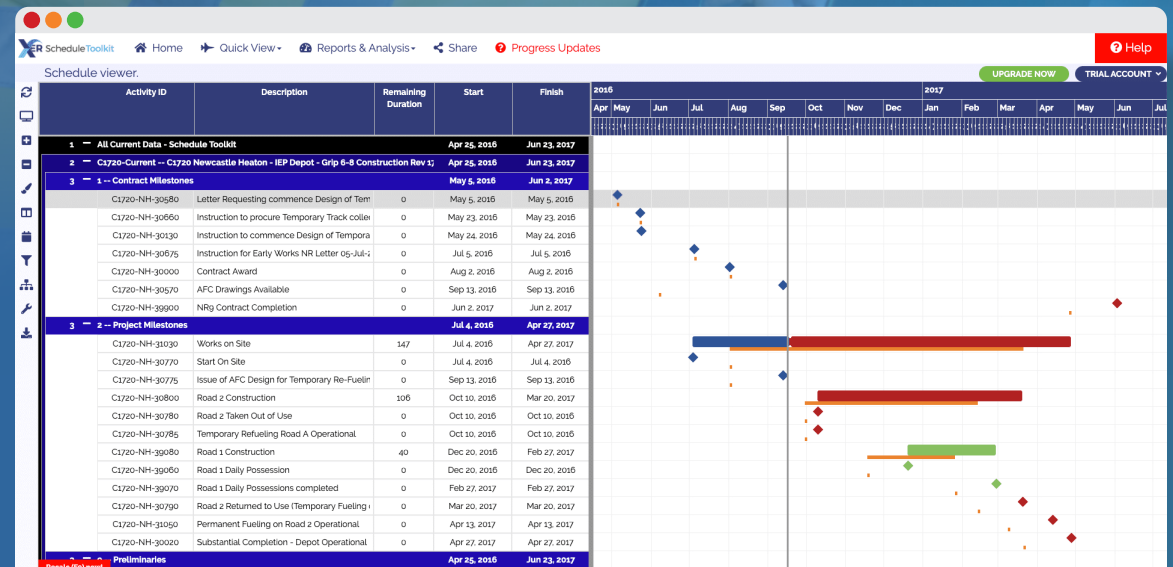



How reliable is your Contractors Programme?

Our schedule quality tool allows you to set your own parameters, incorporate contract restrictions and check the programme compliance with a specific contract such as NEC3.

XER Schedule Toolkit produces a comprehensive output report, detailing all schedule deficiencies that can be used to analyse and where appropriate resolve problems.






Forensically compare Project Schedules in Seconds

XER Schedule Toolkit provides a detailed comparison and trend report between multiple versions of a project schedule.

The software produces a wide-ranging report detailing differences between dates, durations, logic, descriptions, resource assignments and even the activity code assignments.

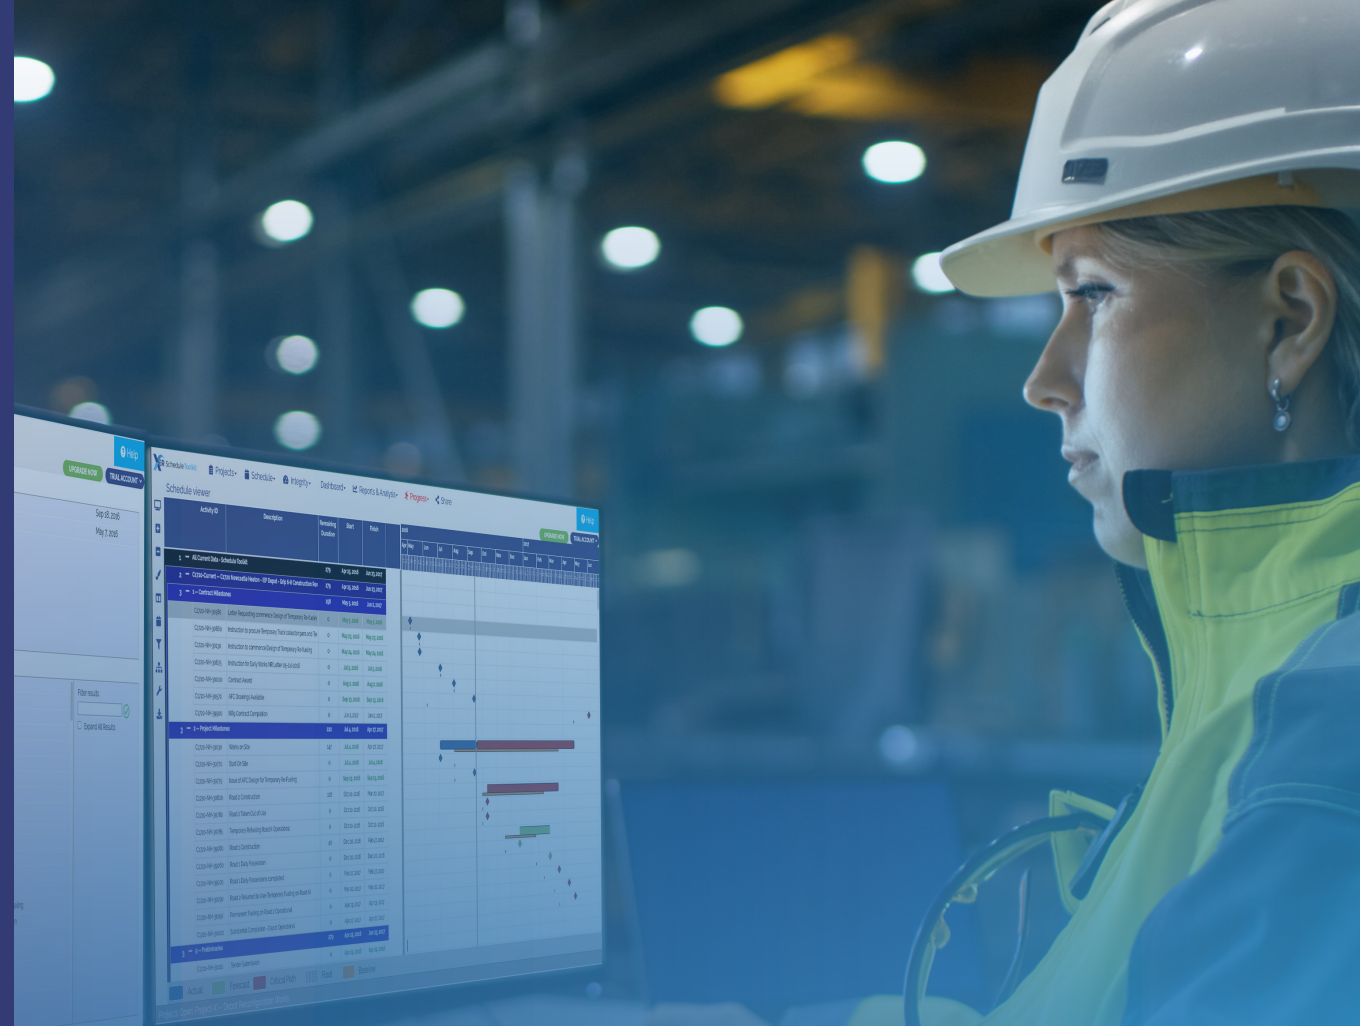

XER Schedule Toolkit Home Quick View Reports & Analysis Share Progress Updates [UPGRADE NOW](#) [TRIAL ACCOUNT](#) [Help](#)

Project comparison

Projects to Compare	Start Date
1 Project-X Depot Reconfiguration Works	Sep 18, 2016
2 C1720-Rev 10a-1 Rev 10a C14 Heaton - Construction Clause 14 Submission Including costs loaded	May 7, 2016

Category

- Project
- WBS
- Task
- Logic
- Activity Codes
- Budget Cost - Labour
- Budget Cost - Equipment
- Budget Cost - Expenses
- Budget Cost - Materials
- Budget Units - Labour
- Budget Units - Equipment
- Budget Units - Expenses
- Budget Units - Materials

Changes Identified

- Data Date
- Project ID Code
- Project Description
- Nr of WBS Elements
- Activities - Total
- Actual Units
- Remaining Units
- At Completion Units
- Budgeted Cost
- Actual Cost
- Remaining Cost
- At Completion Cost
- Relationships Count - Total
- Relationships Count - Start to Start

View Detail

- Project Check - Data Date
- 1 Sep 18, 2016
- 2 May 7, 2016 ---- 1-134 days

Filter results:
 Expand All Results



Ensure Everyone is working to the latest progress schedule

Set up various schedule layouts, filters & dashboard reports at the start of a project.

Create share groups for the whole team or personalised to a specific department or individual.

Use the 'share' feature to give everyone instant access to view and analyse the contemporary project schedule in a format that is relevant and useful for them.

A screenshot of the XER Schedule Toolkit software interface. The window title is "XER Schedule Toolkit". The main content area shows "PROJECT SHARE STATUS" for project "1234ABCD" with the name "Ravine - Plant Expansion & Modernization". There are two sections: "SHARE-TEAMS" and "SHARE-TEAM MEMBERS".

SHARE-TEAMS			SHARE-TEAM MEMBERS:		
	Share?	Share Units?	Share Cost?	TEAM: Example Share-Team: Designs	Account Status
Example Share-Team: Designs	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	designer_1@xertoolkit.co.uk	Invite?
Example Share-Team: Installers	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	designer_2@xertoolkit.co.uk	Invite?
				designer_3@xertoolkit.co.uk	Invite?



Request progress updates at the click of a button

Provide your work package managers with the capability to provide progress updates for the activities which they are responsible for delivering.

Following each progress update, you can simply load the latest version of the project into XER Schedule Toolkit and everyone is instantly aligned.



The screenshot displays the XER Schedule Toolkit interface. At the top, there are navigation tabs: Home, Quick View, Reports & Analysis, Share, and Progress Updates. A red 'Help' button is in the top right corner. Below the navigation is a 'Schedule viewer' section with a '2019' calendar header and a 'UPGRADE NOW' button. The main area is a Gantt chart with columns for days of the month (1-30) and rows for activities. Each activity row includes an 'Update Now' button. The activities are organized into a hierarchical tree structure.

Activity ID	Description	Start	Fin	2019
1 -- All Current Data - Schedule Toolkit		Jan 1, 2019	Apr 30	
2 -- EC00630 -- Saratoga Senior Community		Jan 1, 2019	Apr 30	
3 -- 1 -- Building 1		Jan 1, 2019	Mar 18	
4 -- 1 -- Structure		Jan 1, 2019	Mar 18	
Update Now	EC1010 Curbs & Paving	Jan 1, 2019	Jan 1	
Update Now	EC1090 Building Pad Including UG Utils	Jan 1, 2019	Mar 18	
3 -- 2 -- Building 2		Jan 28, 2019	Apr 12	
4 -- 1 -- Structure		Jan 28, 2019	Apr 12	
Update Now	EC1150 Building Slab Incl. UG Utils	Jan 28, 2019	Apr 12	
3 -- 5 -- Garage 1		Jan 1, 2019	Apr 26	
Update Now	EC1430 Shop Drawings, Review & Approval	Jan 1, 2019	Apr 26	
Update Now	EC1420 Start Garage	Jan 1, 2019	Jan 1	
3 -- 6 -- Garage 2		Jan 1, 2019	Apr 24	
Update Now	EC1030 Shop Drawings, Review and Approval	Jan 1, 2019	Apr 24	
Update Now	EC1020 Start Garage	Jan 1, 2019	Jan 1	
3 -- 7 -- Roads, Utilities & Pavers		Jan 1, 2019	Apr 30	
Update Now	EC1100 Storm Drainage Site Work	Jan 1, 2019	Apr 24	
Update Now	EC1040 Site Cleanup	Jan 1, 2019	Apr 24	
Update Now	EC1000 Curbs & Paving	Jan 1, 2019	Apr 24	
Update Now	EC1050 Site Cleanup	Jan 1, 2019	Apr 19	
Update Now	EC1110 Site Electrical Work & Temp Power	Jan 1, 2019	Jan 18	

Our wide range of plans ensure that there is a package to cater for every need including freelance planners, small and medium enterprises, projects and large corporations.

Individual Licence Package

1x Admin Licence
2x Read only Licence

£299/Year
£39.99/Month

Team Licence Package

2x Admin Licence
4x Read only Licence

£579/Year
£74/Month

Small Project Licence Package

4x Admin Licence
8x Read only Licence

£999/Year
£139/Month

Medium Project Licence Package

8x Admin Licence
16x Read only Licence

£1,999/Year
£259/Month

Mega Project Licence Package

20x Admin Licence
40x Read only Licence

£4,999/Year
£599/Month

Enterprise Licence Package

40x Admin Licence
200x Read only Licence

**Contact us
for pricing**

LICENCE FEATURES	READ ONLY	STANDARD ADMIN	ENTERPRISE
IT INFRASTRUCTURE & SECURITY FEATURES			
Customer - Dedicated Server			✓
Can Implement 2 Factor Authorisation (2FA)			✓
Integration with Customer's Single Sign On (SSO)			✓
Customer Logo			✓
Customer Branding			✓
All XER Branding Removed			✓
Server Location	Ireland	Ireland	Customer Choice*
APPLICATION FEATURES			
Bespoke Report Development			✓
Bespoke Dashboard Menu Options			✓
Bespoke Schedule Quality Menu			✓
Export Schedule to PDF			✓
Export Schedule to Excel		✓	✓
Share Projects		✓	✓
Import Primavera P6 (.xer, .xml, and .plft (.mpp, and .mpt) Projects		✓	✓
Import Microsoft Project (.mpp, and .mpt) Projects		✓	✓
Schedule Comparison Analysis	✓	✓	✓
Earned Value Analysis	✓	✓	✓
Calendar Viewer	✓	✓	✓
Full Time Equivalent (FTE) Histogram	✓	✓	✓
Progress Input Facility	✓	✓	✓
Dashboard Report	✓	✓	✓
Schedule Quality Metrics	✓	✓	✓
Individual Account	✓	✓	✓
Schedule Viewer	✓	✓	✓

Get In Touch

Please do not hesitate to contact us, we will be happy to help you with any query you may have

Have a Question?

For all general and technical support queries, send an email to -

 support@xertoolkit.com

Sign up for a free trial

Sign up for a free trial on our website -

 www.xertoolkit.com

  Follow us
